

Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Software Engineering Laboratory

Name: Shamika Mahesh

SRN: PES1UG24AM259

Project: GreenRelief – Disaster Relief Supply & Volunteer Coordinator

Domain: Sustainability & Green Tech

Actors: Relief Volunteer, Disaster Manager

1. Epics and User Stories (Backlog)


The backlog was structured into 3 Epics covering resource coordination, volunteer deployment, and disaster monitoring/sustainability reporting. Each Epic was broken down into 3 User Stories, all assigned a Priority level and Story Points using the Fibonacci scale.

Epic	User Story	Priority	Points
Epic 1: Sustainable Resource & Supply Coordination	Resource Inventory Tracking	High	5
	Resource Request Submission	High	3
	Green Supply Chain Tracking	Medium	8
Epic 2: Volunteer Deployment & Task Management	Volunteer Registration & Skill Mapping	High	3
	Task Assignment	High	5
	Volunteer Check-In / Safety Status	Medium	2
Epic 3: Real-Time Disaster Monitoring & Sustainability Reporting	Live Disaster Zone Mapping	Highest	8
	Sustainability Metrics Dashboard	Medium	5
	Incident Reporting by Volunteers	High	3

Total backlog: 3 Epics, 9 User Stories, 42 story points


2. Jira Screenshots

2.1 Backlog — Epics, User Stories & Story Points

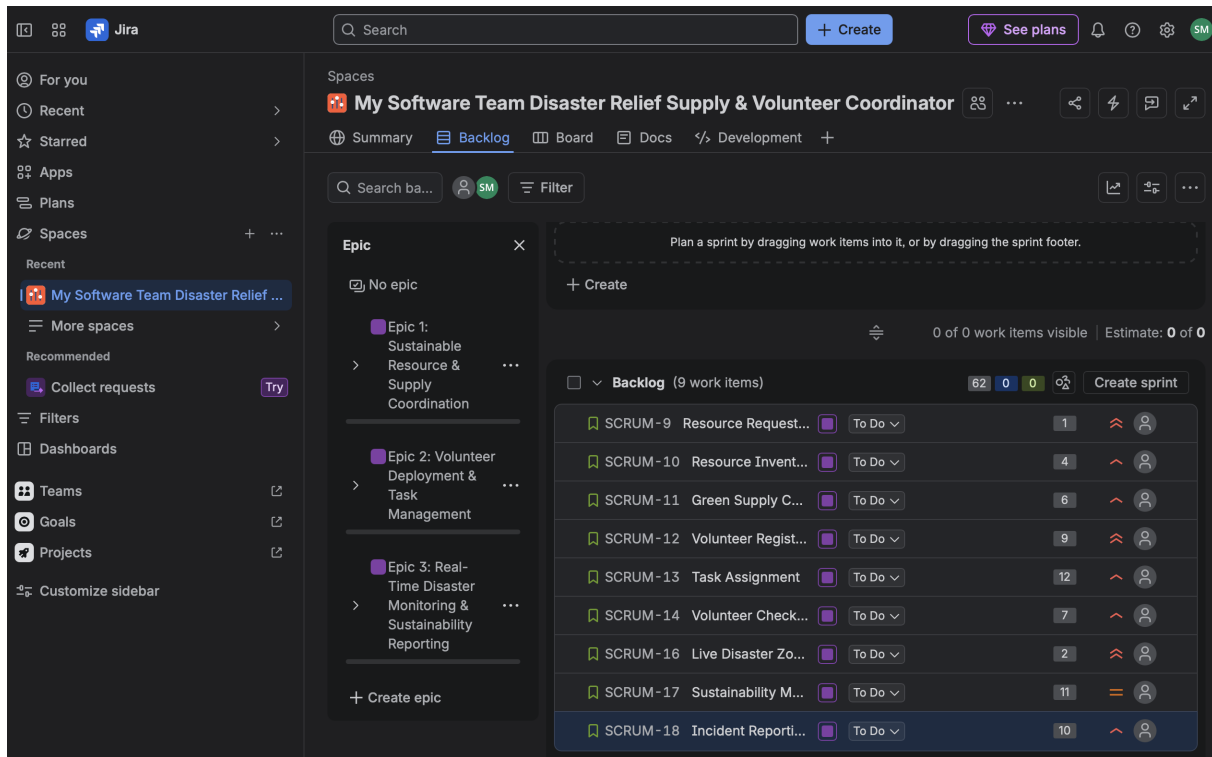


Backlog view showing all 3 Epics, 9 User Stories, and their assigned Story Points.

2.2 Active Sprint Board

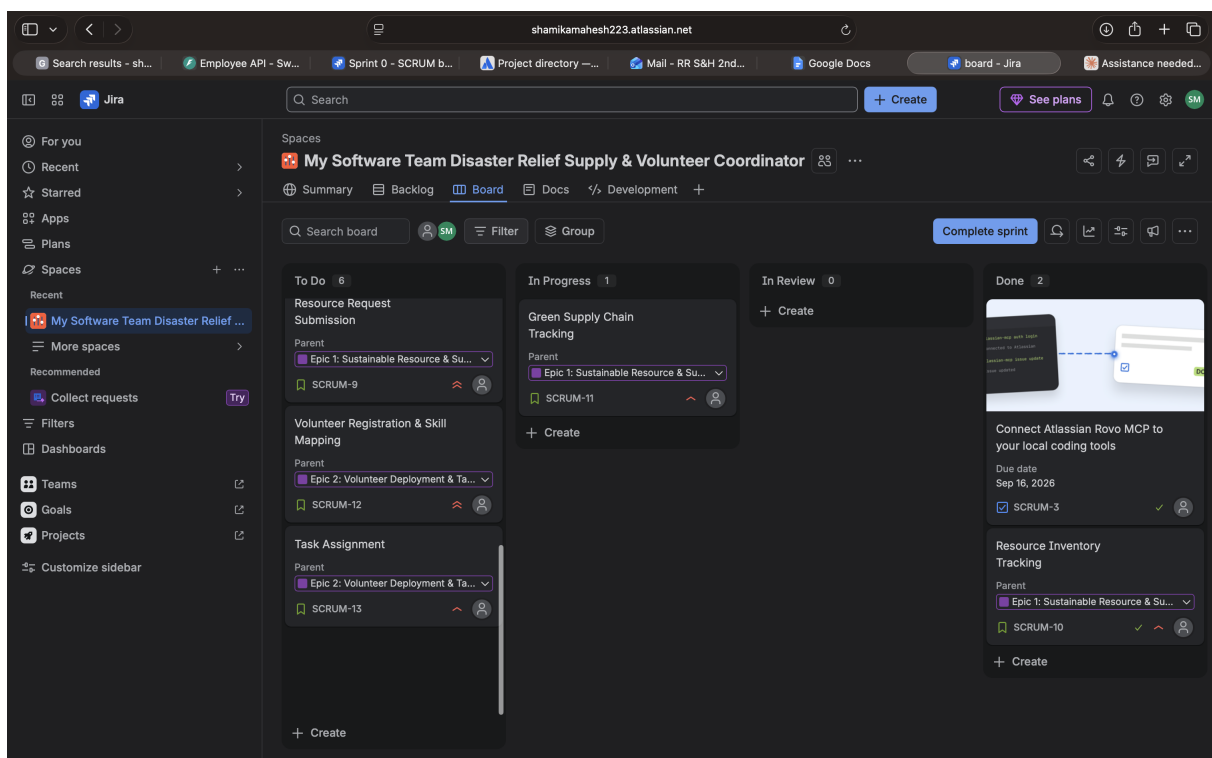

Active Sprint board mid-simulation: stories distributed across To Do, In Progress, and Done columns.

2.3 Burndown Chart

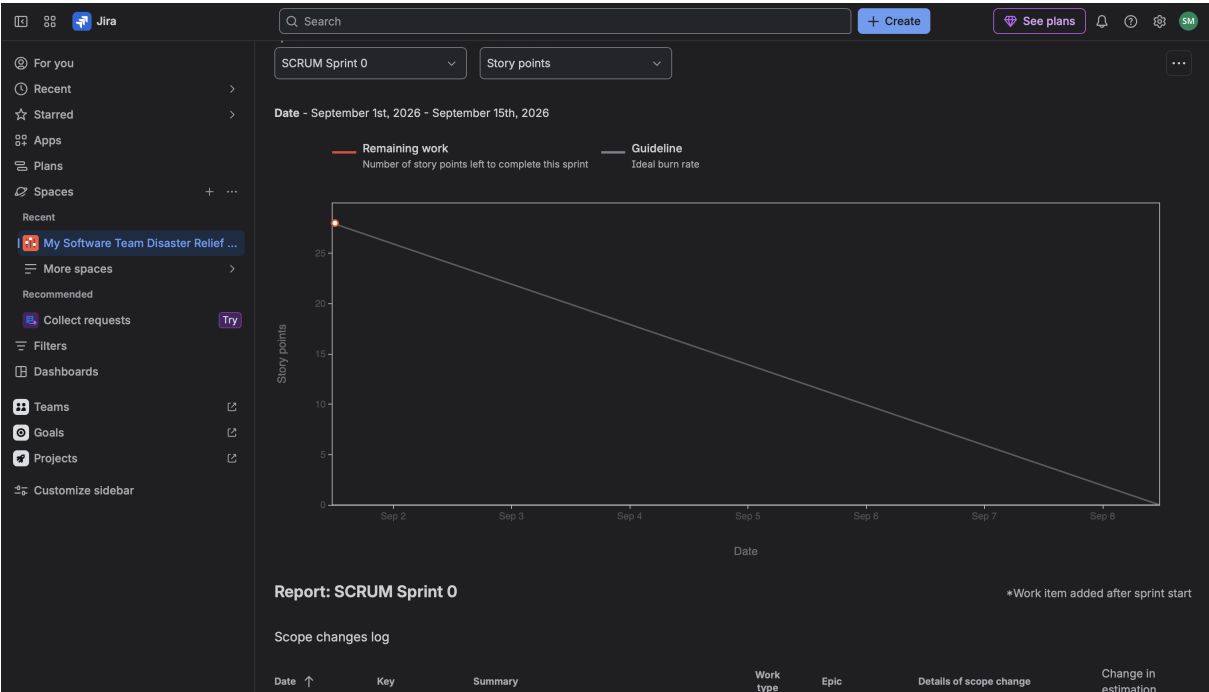


Burndown chart for the sprint, showing the ideal guideline burn rate against total story points.

2.4 Sprint Summary Dashboard



Summary dashboard showing work item breakdown by status, type, and assignee.

2.5 Reports — Cycle Time & Completion Trends

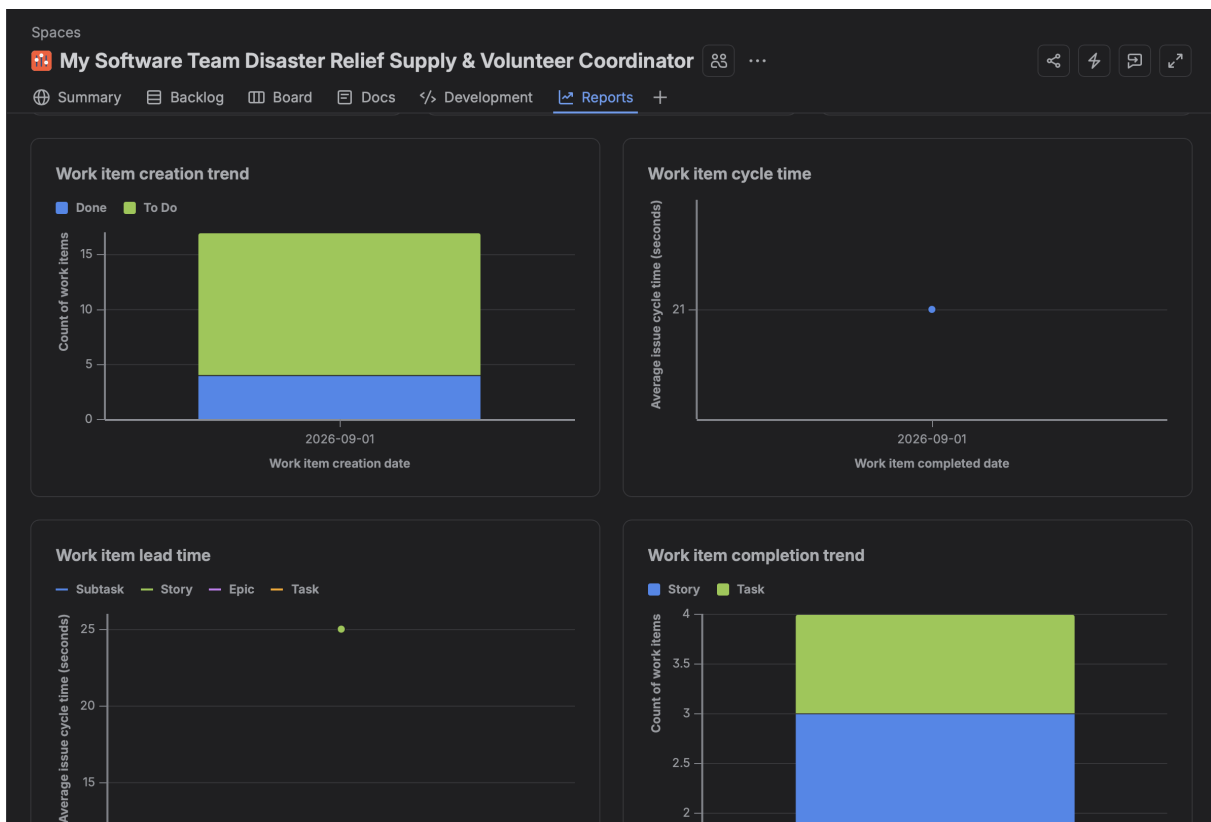

Work item creation trend, cycle time, lead time, and completion trend reports.

2.6 Work Item Details Table

Spaces

My Software Team Disaster Relief Supply & Volunteer Coordinator

Summary Backlog Board Docs Development Reports +

2026-09-01 Work item creation date

2026-09 Work item resolution date

Work item details

Search table

Work item key	Work type	Work item priority	Issue summary
SCRUM-1	Task		Start here: Add your team's work
SCRUM-10	Story	High	Resource Inventory Tracking
SCRUM-11	Story	High	Green Supply Chain Tracking
SCRUM-12	Story	Highest	Volunteer Registration & Skill Mapping
SCRUM-13	Story	High	Task Assignment
SCRUM-14	Story	High	Volunteer Check-In / Safety Status
SCRUM-15	Epic	Medium	Epic 3: Real-Time Disaster Monitoring & Sustainability Reporting
SCRUM-16	Story	Highest	Live Disaster Zone M

Showing

Full work item table with priorities and issue summaries.

3. Reflection Questions

1. Did your estimations reflect the actual effort?

For the most part, yes. Smaller stories such as Volunteer Check-In / Safety Status (2 points) and Resource Request Submission (3 points) moved through the board quickly, which matched their low estimates. Larger stories like Live Disaster Zone Mapping and Green Supply Chain Tracking (8 points each) took noticeably longer to move out of To Do, confirming that the higher-complexity, higher-uncertainty items were estimated appropriately. By the time the sprint board was reviewed, only 2 of the 9 stories had reached Done and 1 was In Progress, suggesting the team's actual velocity for the sprint was lower than the total backlog estimate of 42 points — a realistic outcome for a first sprint where the team is still calibrating its estimation accuracy.

2. Was your backlog well-prioritized?

Yes, prioritization followed the logical dependency order of the scenario. Highest-priority stories — Live Disaster Zone Mapping (Highest) and the core resource/volunteer stories (High) — were placed at the top of the backlog and pulled into the sprint first, since a disaster response system needs situational awareness and basic resource/volunteer coordination before anything else. Medium-priority stories such as the Sustainability Metrics Dashboard and Green Supply Chain Tracking were correctly sequenced later, as they depend on operational data being generated by the higher-priority features first.

3. How did your simulated sprint align with your plan?

The sprint largely followed the intended flow: stories were dragged from the Backlog into Sprint 1, the sprint was started, and cards were progressively moved from To Do to In Progress to Done. The Active Sprint board screenshot shows 6 stories still in To Do, 1 in In Progress, and 2 already in Done — which reflects a typical early-to-mid sprint state rather than a fully completed one. This is a reasonable simulation outcome, since real sprints rarely have all work items complete until closer to the sprint's end date.

4. What insights did the burndown chart give about your team's capacity?

The burndown chart's guideline line shows a steady, linear decrease in remaining story points across the sprint duration — this is the ideal burn rate the team should aim to match. Since only a portion of the stories had reached Done at the point the board was captured, the actual remaining-work line would likely sit above the guideline for the early-to-mid sprint window, which is expected and not necessarily a red flag this early on. It does suggest that for future sprints, the team should either commit to a slightly smaller batch of story points per sprint or break the larger (8-point) stories into smaller sub-tasks so that progress is visible more incrementally rather than in large jumps near the deadline.
